



International School

Capstone Project 1

CMU-SE 450

Project Plan

Version 1.0

Date: Sep 9th, 2026

COVAI
TEST COVERAGE ANALYSIS AND AI-DRIVEN
TEST GENERATION SYSTEM

Created by C1SE.30

Dinh, Huynh Tan

Phuc, Tran Huu

Quy, Nguyen Duy

Thuan, Ngo Huu

Approved by

Man, Nguyen Duc, Ph.D.

Project Plan Review Panel Representative:

Name	Signature	Date
------	-----------	------

Capstone Project 1- Mentor:

Name	Signature	Date
------	-----------	------

PROJECT INFORMATION

Project acronym	COVAI		
Project Title	Test Coverage Analysis and AI-Driven Test Generation System		
Start Date	Aug 10, 2026	End Date	Dec 12, 2026
Lead Institution	International School, Duy Tan University		
Project Mentor	Man, Nguyen Duc, Ph.D.		
Scrum master / Project Leader & contact details	Dinh, Huynh Tan Email: huynhtandinh.dev@gmail.com Tel: 0365 472 162 ID: 29219052500		
Partner Organization	Duy Tan University		
Project Web URL			
Team members	Name	Email	Tel
29219052500	Dinh, Huynh Tan	huynhtandinh.dev@gmail.com	0365472162
29211458179	Phuc, Tran Huu	phuc12435az@gmail.com	0842644169
29211158823	Quy, Nguyen Duy	quylavip333@gmail.com	0334814522
29219065178	Thuan, Huu Ngo	thuanhuugl@gmail.com	0385591447

DOCUMENT APPROVALS

The following signatures are required for approval of this document.

Dinh, Huynh Tan Student ID: 29219052500 <i>Scrum Master</i>	Signature	Date
Phuc, Tran Huu Student ID: 29211458179 <i>Team Member</i>	Signature	Date
Quy, Nguyen Duy Student ID: 29211158823 <i>Team Member</i>	Signature	Date
Thuan, Ngo Huu Student ID: 29219065178 <i>Team Member</i>	Signature	Date

PROJECT PLAN DOCUMENT

Document Title	Project Plan Document		
Author(s)	Dinh, Huynh Tan		
Role	Scrum Master		
Date	August 10, 2026	File name:	C1SE.30_ProjectPlan_v1.1.docx

REVISION HISTORY

Version	Date	Comments	Author
1.0	Sep 09, 2026	Initial Document	Dinh
1.1	Sep 10, 2026	Update Document	Dinh

TABLE OF CONTENTS

1. Introduction	1
1.1. Purpose	1
1.2. Project Overview	1
1.3. Project Deliverable	2
2. Team Organization	3
2.1. Scrum Team Information	3
2.2. Role and Responsibility	3
2.3. Communication Methodology	4
3. Development	6
4. Schedule and Cost	7
4.1. Detailed Schedule	7
4.2. Cost Person/Hours	9
4.3. Tooling, Infrastructure & Material Expenses	10
4.4. Total Cost Estimate	12
5. Project Risk	14
6. Deliverables	17

LIST OF TABLES

Table 1 - Scrum Team Organization	3
Table 2 - Role and Responsibilities.....	3
Table 3 - Communication Methodology	4
Table 4 - Communication and Report	5
Table 5 - Detailed Schedule	7
Table 6 - Cost of person/hours	9
Table 7 - Labor & Resource Parameters	12
Table 8 - Total Project Cost Estimation	13
Table 9 - Risk Rating.....	14
Table 10 - Project Risk	14
Table 11 - Deliverables	17

1. Introduction

1.1. Purpose

The purpose of this document is to provide a comprehensive project management and development plan for the COVAI – Software Testing and AI Chatbot Trustworthiness Evaluation System.

This document defines the project organization, team responsibilities, communication methods, development methodology, implementation schedule, resource allocation, risk management, and project deliverables.

The project plan serves as a guideline for the COVAI development team to coordinate activities, monitor project progress, manage technical risks, and ensure that the project is completed within the planned academic schedule.

The main goal is to successfully develop an AI-driven software quality platform that supports automated software testing, test coverage analysis, code structure analysis, AI-assisted test generation, and project-specific evaluation of internal AI chatbot trustworthiness.

1.2. Project Overview

The detailed project background, problem statement, proposed solution, system scope, architecture, functional requirements, and non-functional requirements are defined in:

C1SE.30_Proposal_ver1.2.docx

- COVAI is an AI-driven software quality platform that provides two major capabilities:
- Software Testing and Quality Analysis: source-code ingestion, testing-framework detection, isolated test execution, coverage analysis, Control Flow Graph analysis, Cyclomatic Complexity analysis, and AI-assisted test generation.
- AI Chatbot Trustworthiness Evaluation: project-specific evaluation of internal AI chatbots using business rules, knowledge bases, API specifications, expected behaviors, and measurable trustworthiness criteria.
- COVAI initially focuses on JavaScript/TypeScript projects and supports selected testing frameworks including Jest, Vitest, Supertest, Playwright, and Cypress.

1.3. Project Deliverable

Primary Software Deliverable

A functional academic prototype of the COVAI platform containing the following major capabilities:

- User authentication and project management.
- Local source-code upload and GitHub repository import.
- Project snapshot management.
- Automatic testing-framework detection.
- Docker-based isolated test execution.
- Test coverage analysis.
- Control Flow Graph and Cyclomatic Complexity analysis.
- AI-assisted test generation.
- Multi-framework testing support.
- GitHub webhook automation.
- Background job processing and notifications.
- AI evaluation knowledge ingestion.
- Evaluation profile configuration.
- Benchmark and evaluation scenario generation.
- Internal AI chatbot evaluation.
- Trustworthiness scoring, diagnosis, comparison, and reporting.

Supporting Deliverables:

- Final Report Submission (Full)
- Project Proposal
- Project Plan (Project Plan, Sprint Plan)
- Requirements Engineering Documents (SRS, User Stories, Product Backlog)
- System Architecture Document (System Design, Database Design, Algorithm Design)
- UI Design Document
- Software Test Plan
- Test Cases & Test Data
- Test Report & Bug Report
- Management Documents (Meeting Minutes, Teamwork Evidence)

- Code Standards and Project Standards
- Reflection & 360 Peer Evaluation
- Technical Report (Scientific Paper / Project Summary Paper)
- Source Code Repository
- Revised Documents and Presentation Slides

2. Team Organization

2.1. Scrum Team Information

Table 1 - Scrum Team Organization

Full Name	Phone	Email	Position
Nguyen Duc Man, Ph.D.	0904235945	mannd@duytan.edu.vn	Project Mentor
Huynh Tan Dinh	0365472162	huynhtandinh.dev@gmail.com	Project Leader / Scrum Master / AI & Backend Lead
Tran Huu Phuc	0842644169	phuc12435az@gmail.com	Backend & Integration Developer
Nguyen Duy Quy	0334814522	quylavip333@gmail.com	Data & Full-Stack Developer
Ngo Huu Thuan	0385591447	thuanhuugl@gmail.com	Frontend Lead / Full-Stack Developer

2.2. Role and Responsibility

Table 2 - Role and Responsibilities.

Full Name	Project Role	Primary Responsibilities
Nguyen Duc Man, Ph.D.	Project Mentor	Guide project direction, review milestones, monitor progress

Full Name	Project Role	Primary Responsibilities
Huynh Tan Dinh	Project Leader / Scrum Master / AI & Backend Lead	System architecture, backend core services, AI test generation pipeline, and CI/CD infrastructure
Tran Huu Phuc	Backend & Integration Developer	Business logic APIs, database schema design, system integration, and end-to-end testing
Nguyen Duy Quy	Data & Full-Stack Developer	Database query optimization, data analysis services, API integration, and user interface modules
Ngo Huu Thuan	Frontend Lead / Full-Stack Developer	Frontend architecture (React dashboard), UI/UX design implementation, state management, and client performance

2.3. Communication Methodology

Table 3 - Communication Methodology

Audience	Topic	Frequency	Method
Mentor & Project Team	Project progress, technical issues, scope review, research direction	Weekly	Face-to-face / Online Meeting / Email
Project Team	Sprint progress, blockers, task coordination	Daily	Messenger / Zalo / Jira
Project Team	Source code, pull requests, issue tracking	Continuous	GitHub
Project Team	Sprint planning and backlog management	Beginning of each Sprint	Jira / Meeting

Audience	Topic	Frequency	Method
Project Team & Mentor	Sprint result/demo/review	End of each Sprint	Meeting / Demo

2.4. Communication and Report

Table 4 - Communication and Report

Type of Communication	Methods / Tools	Frequency	Information	People
Daily Scrum	Face-to-face / Discord	Every 1–2 days	Completed tasks, current tasks, blockers and required support	Project Team
Sprint Planning	Face-to-face / Online Meeting + Jira	Beginning of each 2-week Sprint	Select backlog items, estimate workload, assign tasks and define Sprint Goal	Project Team
Technical Review	GitHub / Discord	During Sprint	Review architecture, code, pull requests and technical issues	Project Team
Sprint Review	Demo / Meeting	End of each Sprint	Demonstrate completed functions and collect feedback	Team & Mentor
Sprint Retrospective	Meeting	End of each Sprint	Review what went well, problems encountered and improvements for the next Sprint	Project Team
Project Progress Report	Document / Meeting	Weekly	Overall progress, risks, completed work and next activities	Project Leader & Mentor

3. Development

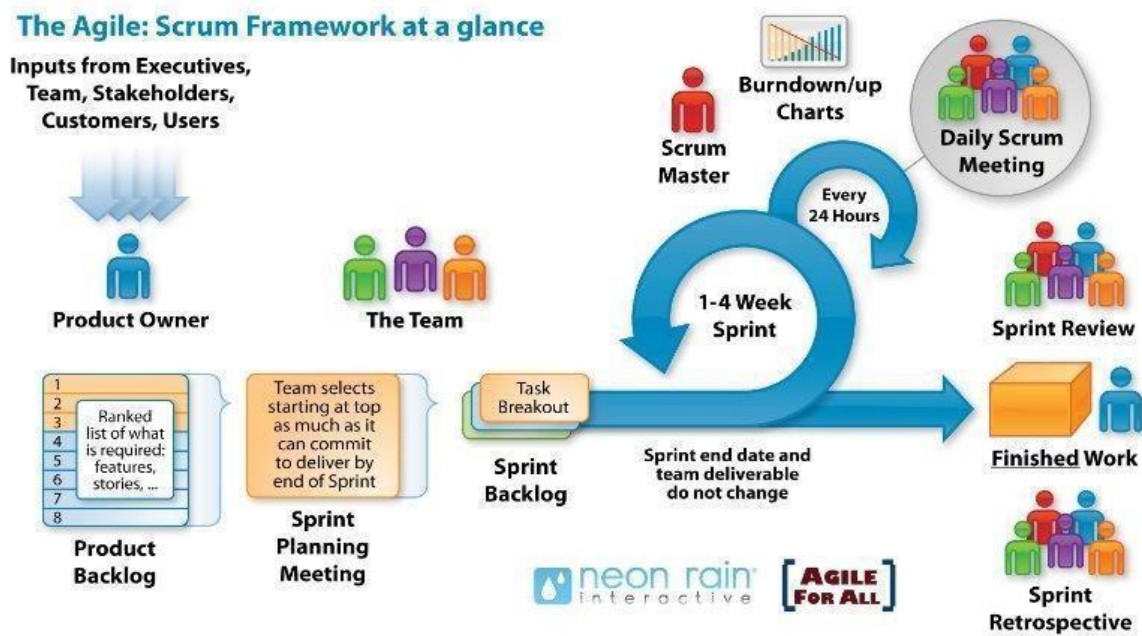


Figure 1 – Scrum Process

The COVAI project follows the Agile Scrum methodology with iterative and incremental development.

The project contains several interdependent technical components, including frontend interfaces, backend APIs, Docker-based test execution, source-code analysis, multiple testing frameworks, AI-assisted test generation, GitHub automation, and AI chatbot trustworthiness evaluation.

Therefore, the system is divided into manageable development Sprints. Each Sprint defines a specific goal and produces an increment that can be tested, reviewed, and improved before proceeding to the next phase.

Scrum Activities:

- Product Backlog: Stores project requirements, user stories, technical tasks and research tasks.
- Sprint Planning: Selects backlog items and defines the Sprint Goal.
- Development: Implements frontend, backend, testing, AI and integration tasks.
- Daily Scrum: Tracks current progress and blockers.
- Testing: Tests completed functionality during each Sprint.
- Sprint Review: Demonstrates completed features.

- Sprint Retrospective: Identifies problems and improvements for the next Sprint.

Benefits of Scrum for COVAI:

- Supports changing technical and research requirements.
- Allows complex features to be implemented incrementally.
- Identifies integration problems early.
- Supports frequent testing and feedback.
- Reduces risk when integrating AI and multiple testing frameworks.
- Enables the team to prioritize core features under the limited Capstone schedule.

4. Schedule and Cost

4.1. Detailed Schedule

Table 5 - Detailed Schedule

No.	Task Name	Duration (Days)	Start Date	End Date	Assigned To
—	Project Timeline	131	Aug 10, 2026	Dec 26, 2026	
1	Initial Project Phase	35	Aug 10, 2026	Sep 14, 2026	
1.1	Kick-off Meeting	1	Aug 10, 2026	Aug 10, 2026	All
1.2	Discuss Project Idea	2	Aug 11, 2026	Aug 12, 2026	All
1.3	Proposal Document	4	Aug 13, 2026	Aug 16, 2026	All
1.4	Project Plan Document	3	Aug 17, 2026	Aug 19, 2026	Dinh
1.5	Product Backlog	3	Aug 20, 2026	Aug 22, 2026	Thuan
1.6	User Stories	3	Aug 23, 2026	Aug 25, 2026	Dinh
1.7	Software Requirements Specification (SRS)	5	Aug 26, 2026	Aug 30, 2026	Quy, Phuc, Dinh

No.	Task Name	Duration (Days)	Start Date	End Date	Assigned To
1.8	System Architecture Design	4	Aug 31, 2026	Sep 03, 2026	All
1.9	Database Design	3	Sep 04, 2026	Sep 06, 2026	Thuan
1.10	User Interface Design	4	Sep 07, 2026	Sep 10, 2026	Thuan
1.11	Sprint Plan	3	Sep 11, 2026	Sep 13, 2026	All
2	Development Phase 1	48	Sep 14, 2026	Oct 31, 2026	
2.1	Sprint 1 – Environment Setup, Authentication & Project Management	14	Sep 14, 2026	Sep 27, 2026	All
2.2	Sprint 2 – Source Ingestion, Test Execution & Coverage Analysis	14	Sep 28, 2026	Oct 11, 2026	All
2.3	Sprint 3 – Code Analysis, Multi-Test Framework Support & AI Test Generation	14	Oct 12, 2026	Oct 25, 2026	All
2.4	Sprint 4 – GitHub Automation, Monitoring & System Integration	6	Oct 26, 2026	Oct 31, 2026	All

No.	Task Name	Duration (Days)	Start Date	End Date	Assigned To
3	Midterm Report	7	Nov 01, 2026	Nov 07, 2026	All
4	Development Phase 2	32	Nov 08, 2026	Dec 09, 2026	
4.1	Sprint 5 – AI Chatbot Trustworthiness Evaluation Module	14	Nov 08, 2026	Nov 21, 2026	All
4.2	Sprint 6 – End-to-End System Testing & Quality Assurance	7	Nov 22, 2026	Nov 28, 2026	All
4.3	Sprint 7 – System Deployment, Final Fixes & Project Delivery	11	Nov 29, 2026	Dec 09, 2026	All
5	Final Document Submission	4	Dec 10, 2026	Dec 13, 2026	All
6	Project Retrospective Meeting	3	Dec 14, 2026	Dec 16, 2026	All
7	Capstone Defense	10	Dec 17, 2026	Dec 26, 2026	All

4.2 Cost Person/Hours

Table 6 - Cost of person/hours

Team Member	Role	Assigned Days	Calculation (6 hours/day)	Total Effort (Hours)
Dinh, Huynh Tan	Team Leader / AI & Backend Lead	107	107 x 6	642

Thuan, Ngo Huu	Frontend Lead, Full-Stack Developer	107	107 x 6	642
Quy, Nguyen Duy	Data & Full-Stack Developer	107	107 x 6	642
Phuc, Tran Huu	Backend & Integration Developer	107	107 x 6	642

Non-Billable Academic Labor:

- Since COVAI is an academic Capstone project, student labor is considered non-billable academic effort and is therefore not included as a direct monetary project cost.

Standard Effort Unit:

- Standard working effort: Daily Rate = 6 hours/day/member.

Effort Breakdown by Member:

$$Effort_{Each\ member} = 107\ days * 6\ hours/day = 642\ hours$$

Total Project Effort:

$$Total\ Effor = 642 * 4 = 2,568\ man - hours$$

Deliverables Covered:

The committed 2,568 man-hours encompass all scheduled iterations including Core Development (Sprints 1–4), Midterm Review, AI Evaluation Integration (Sprint 5), System Testing & QA (Sprint 6), Deployment & Release (Sprint 7), Documentation, and Capstone Defense preparation.

4.3 Tooling, Infrastructure & Material Expenses

Category	Item & Description	Pricing Model / Status	Estimated Cost (VND)
Hardware	Personal development machines (Laptops/PCs)	Existing student-owned equipment	0 VND
Infrastructure	Cloud VPS / Database hosting	Paid cloud instance (monthly/quarterly)	250,000 – 400,000 VND

Category	Item & Description	Pricing Model / Status	Estimated Cost (VND)
	(Testing & Demo)		
Domain & Network	Custom domain name & SSL	1-year registration / Let's Encrypt	150,000 – 250,000 VND
AI Services	Gemini API & LLM integration	Google AI Studio (Free tier quota) + buffer pay-as-you-go	100,000 VND
Software & Tools	IDEs, Git repository, Docker, Open-source libs	GitHub Education / Open-source licenses	0 VND
Academic Deliverables	Poster printing, capstone thesis binding, demo materials	Academic submission expenses	200,000 – 300,000 VND
Contingency	Miscellaneous & service overage reserve (~10%)	Contingency buffer	100,000 VND
Total Estimated Budget	All categories combined	—	800,000 – 1,150,000 VND

Hardware & Development Workstations (0 VND):

- All development, testing, and debugging are performed using student-owned personal computers and laptops.
- No institutional capital expenditure is required for workstation hardware.

Cloud Infrastructure & Production Hosting (250,000 - 400,000 VND):

- Procures a lightweight Virtual Private Server (VPS) and cloud database instances (e.g., Ubuntu/Docker environment) for staging, public API testing, and final defense live demo.

- Budget formula: $\text{Cost_Infra} = \text{Monthly Fee} \times \text{Demo Period (approx. 2–3 months)}$.

Domain & Network Configuration (150,000 - 250,000 VND):

- Covers 1-year registration for a custom top-level domain (TLD) to serve public webhooks (GitHub automation) and live production routing.
- Standard SSL/TLS encryption is provisioned via free automated certificates (Let's Encrypt).

AI Services & LLM Integration (100,000 VND):

- Primary development relies on free-tier allowances from Google AI Studio / Gemini API.
- The allocated 100,000 VND serves as a buffer for automated batch-scoring runs, stress benchmarks, and token overages during system integration.

Software, Licenses & Tooling (0 VND):

- Maximizes open-source stacks (React, Node.js, Express, Docker, Jest, Cypress) and student developer packs (GitHub Education, Visual Studio Code) to keep software acquisition expenses at zero.

Academic Deliverables & Defense Expenses (200,000 - 300,000 VND):

- Allocated for professional hard-cover thesis bookbinding, poster printing for academic reviews, and official capstone submission materials.

Contingency Reserve (100,000 VND):

- A standard reserve representing approximately 10% of total direct expenditures, designated to absorb unexpected network bandwidth spikes or cloud storage surcharges.

Total Financial Commitment:

- Total Project Budget = 800,000 - 1,150,000 VND
(Evenly split among team members as a non-reimbursable academic investment).

4.4 Total Cost Estimate

Table 7 - Labor & Resource Parameters

Parameter Description	Value	Unit
Team Size	4	Members

Daily Working Effort	6	Hours/day
Nominal Labor Rate	3	USD/hour
Total Project Effort (4 Members)	2,568	Hours
Direct Operational & Material Budget	50	USD (~1,150,000 VND)

Table 8 - Total Project Cost Estimation

No.	Cost Category	Basis / Rate	Total Amount (USD)
1	Development Labor Effort	2,568 Hours @ 3 USD/Hour	7,704
2	Infrastructure, AI Services & Academic Deliverables	Lump-sum direct costs	50
—	Total Estimated Project Cost	Labor + Direct Costs	7,754

Detailed Formulas & Explanations:

- Total Working Effort = 107 days x 6 hours x 4 members = 2,568 Man-hours.
- Total Labor Cost = 2,568 hours x 3 USD/hour = 7,704 USD.
- Operational & Deliverables Cost = 50 USD (~1,150,000 VND covering VPS, domain, AI quota buffer, and thesis binding).
- Total Project Budget = 7,704 USD + 50 USD = 7,754 USD.

Note on Academic Context:

Because COVAI is an undergraduate capstone project, the calculated labor cost (7,754 USD) represents a nominal academic valuation. The actual cash outlay required from the team is strictly limited to the direct operational cost of approximately 50 USD (1,150,000 VND).

5. Project Risk

Table 9 - Risk Rating

Rating	Meaning
L	Low
M	Medium
H	High
E	Extreme / Very High
NA	Not Assessed

Table 10 - Project Risk

Risk	Category	Likelihood	Impact	Mitigation Strategy
AI-generated tests may be incorrect or incomplete	AI / Technical	M	H	Validate generated tests, execute them when possible, and provide fallback/TODO output
Test execution may fail because of dependencies or configuration	Technical	H	H	Use isolated Docker environments, preflight checks, timeout mechanisms and clear logs
Multi-framework support increases system complexity	Technical	M	H	Use framework-specific adapters and prioritize selected frameworks
Large projects may consume excessive computing resources	Performance	M	H	Use job queues, resource/time limits and snapshot reuse

Risk	Category	Likelihood	Impact	Mitigation Strategy
Automated chatbot scoring may be biased or inconsistent	AI / Research	M	H	Prefer deterministic checks, store evaluation evidence, calibrate scoring and compare with human judgments
Ground-truth business rules may be incomplete or outdated	Domain	M	H	Require domain-expert confirmation and version evaluation profiles
Tool/action chatbot evaluation may cause unintended effects	Safety	L	E	Use mocks/sandboxes, non-production accounts, confirmation gates and forbidden-action rules
Sensitive project/evaluation data may be exposed	Security	M	H	Apply authorization, minimize transmitted data and prevent unnecessary external exposure
Limited academic development time	Management	H	H	Prioritize core functions and deliver incrementally through Scrum

Risk	Category	Likelihood	Impact	Mitigation Strategy
Target chatbot may not expose sufficient metadata	Integration	M	M	Use configurable adapters and clearly mark unavailable evaluation evidence

6. Deliverables

Table 11 - Deliverables

No.	Deliverable Item	Corresponding Task / Milestone	Deadline	File Name / Artifact
1	Project Proposal Document	1.3 Proposal Document	Aug 16, 2026	C1SE.30_Proposal_ver1.0.docx
2	Project Plan Document	1.4 Project Plan Document	Aug 19, 2026	C1SE.30_ProjectPlan_ver1.0.docx
3	Product Backlog & User Stories	1.5 & 1.6 Requirements Backlog	Aug 25, 2026	C1SE.30_ProductBacklog_ver1.0.xlsx
4	Software Requirements Specification (SRS)	1.7 Software Requirements Specification	Aug 30, 2026	C1SE.30_SRS_ver1.0.docx
5	System Architecture & Database Design	1.8 System Architecture & 1.9 Database Design	Sep 06, 2026	C1SE.30_Architecture_DB_Design.docx
6	UI/UX Design Prototypes	1.10 User Interface Design	Sep 10, 2026	C1SE.30_Figma_UI_Prototype_Link
7	Sprint Plan (Release 1)	1.11 Sprint Plan	Sep 13, 2026	C1SE.30_SprintPlan_Phase1.xlsx
8	Phase 1 Codebase & Test Engine Release	2. Development Phase 1 (Sprints 1–4)	Oct 31, 2026	GitHub Tag: v0.4-phase1-testing
9	Midterm Presentation & Evaluation Report	3. Midterm Report	Nov 07, 2026	C1SE.30_Midterm_Report_Slide.pptx

No.	Deliverable Item	Corresponding Task / Milestone	Deadline	File Name / Artifact
10	Phase 2 AI Evaluation Engine Release	4. Development Phase 2 (Sprints 5–7)	Dec 09, 2026	GitHub Tag: v1.0-rc-production
11	Final Capstone Thesis & Documentation	5. Final Document Submission	Dec 13, 2026	C1SE.30_Capstone_Thesis_ver1.0.docx
12	Project Retrospective Summary	6. Project Retrospective Meeting	Dec 16, 2026	C1SE.30_Sprint_Retrospective.pdf
13	Capstone Defense Presentation & Live Demo	7. Capstone Defense	Dec 26, 2026	C1SE.30_Final_Defense_Slides.pptx

END

SPRINT 1	
Project Name:	COVAI
Module Name:	Sprint 1
Development Team:	CISE.30
Start Date:	09/14/26
End Date:	09/27/26

No.	Member Name		Estimate (hours)
1	Dinh, Huynh Tan	Dinh	84
2	Quy, Ngyen Duy	Quy	84
3	Thuan, Huu Ngo	Thuan	84
4	Phuc, Tran Huu	Phuc	84
Total			336

	On Time
	Lately
	Early
	Unfinished

Component	No.	Task Name	Resposible Member	Estimate (hours)	14-thg 9-26	15-thg 9-26	16-thg 9-26	17-thg 9-26	18-thg 9-26	19-thg 9-26	20-thg 9-26	21-thg 9-26	22-thg 9-26	23-thg 9-26	24-thg 9-26	25-thg 9-26	26-thg 9-26	27-thg 9-26	28-thg 9-26
Design UI	1	UI Home Page	Thuan	8	6	2	0												
	2	UI Registration	Phuc	8	6	2	0												
	3	UI Login	Dinh	8	6	2	0												
	5	UI Forgot Password	Quy	8	6	2	0												
	4	UI Landscape	Dinh	8	-	4	4	0											
	6	UI Profile User	Phuc	8	-	4	4	0											
	7	UI GitHub Repository	Thuan	8	-	4	4	0											
	8	UI Project	Thuan	8	-	-	2	-	-	6	0								
	9	UI Snapshot	Phuc	8	-	-	-	6	2	0									
Database	10	Design database	Quy, Thuan	24	-	-	-	12	12	0									
Front end	11	(Front-end) Homepage	Quy	8	-	4	4	0											
	15	(Front-end) Forgot Password	Dinh	8	-	-	2	6	0										
	12	(Front-end) Landscape	Quy	8	-	-	2	-	-	6	0								
	14	(Front-end) Login	Phuc	8	-	-	-	-	4	4	0								
	16	(Front-end) GitHub Repository	Phuc	8	-	-	2	-	-	2	4	0							
	13	(Front-end) Registration	Thuan	8	-	-	-	-	-	-	6	2	0						
Back end	17	(Front-end) Project Management	Quy	8	-	-	-	-	-	-	6	2	0						
	18	(Back-end) Forgot Password	Dinh	16	-	-	-	-	6	6	4	0							
	19	(Back-end) Reset Password	Dinh	16	-	-	-	-	-	-	2	6	6	2	0				
	20	(Back-end) Registration	Phuc	16	-	-	-	-	-	-	2	6	6	2	0				
	21	(Back-end) Login	Thuan	16	-	-	-	-	-	-	-	4	6	6	0				
	22	(Back-end) Profile	Quy	16	-	-	-	-	-	-	-	4	6	6	0				
	23	(Back-end) GitHub Repository	Dinh	16	-	-	-	-	-	-	-	-	4	6	6	0			
	24	(Back-end) Environment Setup	Phuc	16	-	-	-	-	-	-	-	-	4	6	4	2	0		
	25	(Back-end) Authentication Middleware	Thuan	16	-	-	-	-	-	-	-	-	-	6	6	4	0		
	26	(Back-end) Snapshot Management	Quy	16	-	-	-	-	-	-	-	-	-	6	6	4	0		
Testing and fix bug	28	Design Test Case for Login	Phuc	4	-	-	-	-	-	-	-	-	-	-	-	2	2	0	
	31	Design Test Case for Profile	Dinh	4	-	-	-	-	-	-	-	-	-	-	-	-	4	0	
	27	Design Test Case for Registration	Dinh	4	-	-	-	-	-	-	-	-	-	-	-	-	2	2	0
	29	Design Test Case for Forgot Password	Thuan	4	-	-	-	-	-	-	-	-	-	-	-	-	2	2	0
	30	Design Test Case for Reset Password	Phuc	4	-	-	-	-	-	-	-	-	-	-	-	-	2	2	0
	32	Design Test Case for Homepage	Thuan	4	-	-	-	-	-	-	-	-	-	-	-	-	-	4	0
	33	Design Test Case for Landscape	Quy	4	-	-	-	-	-	-	-	-	-	-	-	-	2	2	0
	34	Design Test Case for GitHub Repository	Dinh	4	-	-	-	-	-	-	-	-	-	-	-	-	-	4	0
	35	Design Test Case for Project Management	Quy	4	-	-	-	-	-	-	-	-	-	-	-	-	-	4	0
	36	Design Test Case for Snapshot	Phuc	4	-	-	-	-	-	-	-	-	-	-	-	-	-	4	0
			TOTAL	336	24	24	24	24	24	24	24	24	24	24	24	24	24	24	-
			REMAIN	336	312	288	264	240	216	192	168	144	120	96	72	48	24	0	-

SPRINT 1

Project Name:	COVAI
Module Name:	Sprint 1
Development Team:	C1SE.30
Start Date:	09/14/26
End Date:	09/27/26

No.	Member Name		Estimate
1	Dinh, Huynh Tan	Dinh	84
2	Quy, Ngyen Duy	Quy	84
3	Thuan, Huu Ngo	Thuan	84
4	Phuc, Tran Huu	Phuc	84
Total			336

	On Time
	Lately
	Early
	Unfinished

[illegible]

Burn down chart Sprint 1

Estimate	Actual	Date
336	336	14-thg 9-26
312	336	14-thg 9-26
288	336	15-thg 9-26
264	336	16-thg 9-26
240	336	17-thg 9-26
216	336	18-thg 9-26
192	336	19-thg 9-26
168	336	20-thg 9-26
144	336	21-thg 9-26
120	336	22-thg 9-26
96	336	23-thg 9-26
72	336	24-thg 9-26
48	336	25-thg 9-26
24	336	26-thg 9-26
0	336	27-thg 9-26

